

Field Report No.:				16	
SP&A Project No: 22.331			Report Date: 12-13-2024		Time: 9:30AM
Project: Gales Ferry School (Name & Location) 1854 CT-12 Gales Ferry, CT 06335 General Contractor: The Imperial Company, Inc.					
Weather		Site Conditions		Day of Week	
☐ Temp. Range: 48° ☒ Clear ☐ Rain ☐ Foggy ☐ Warm ☐ Overcast ☐ Snow ☐ Cold ☐ Hot		☒ Clear ☐ Dusty ☐ Muddy ☐ Windy ☐ Other		☐ Monday ☐ Thursday ☐ Tuesday ☒ Friday ☐ Wednesday ☐ Saturday	
Type of Work Observed Being Performed					
1	☐	Site work	7	☐	General Trades/Drywall
2	☐	Demolition	8	☐	Windows & Doors
3	☐	Concrete	9	☐	Roofing
4	☐	Masonry	10	☐	Flooring
5	☐	Steel/Misc. Metals	11	☐	Pool
6	☐	Carpentry/Casework/ Mill Work	12	☐	Painting/Interior Finishes
13	☐	Specialties/ Food Service	14	☐	Elevators
15	☐	Plumbing	16	☐	HVAC
17	☐	Electrical	18	☐	Temperature Controls/BMS
19	☐	Sprinkler	20	☒	Finish metal
21	☐	Iron workers	22	☐	Tester (Tri-state)
23	☐	Audio Vis/Low Volt	24	☐	Other:
Work Performed at time of site visit:					
- Approximate number of workers on site – 4 - Installing panels between the Gymnasium & the gable with mechanical louvers on roof D. See attached photo.					
General Remarks:					
- Panels that were installed and have short screws need to be replaced need to be observed for the correct screw length by Garland & SPA in areas where the underside decking is not visible. - Tentative schedule handed at last week's site visit is attached. - Discussed during the site visit was how the rake boards meeting with the new roof panels. Imperial to send an RFI. See attached photo. - For record, the following rooms active leaks and most were reviewed during the site visit – • Library (see attached photo) • Hallway near gym • 236 x2 • 233 • 231 • 227 (see attached photo) • 226 • 218					
Visitors:					
- None.					
Construction Administrator: Steven June					12/19/2024
			(Print Name)		(Date)
Copies To:		☐ CA ☐ Architect ☒ Contractor ☒ Owners			

PHOTOS (see attached photos);

Library roof leaks



Room 227 roof leaks




Roof D – Roof D installation tentatively scheduled to continue work 12/21 (see attached tentative schedule)



Roof D – In garland's hands to come up with a solution for the rakes butting against the roof panels



Tentative schedule presented at the 12/13 meeting.

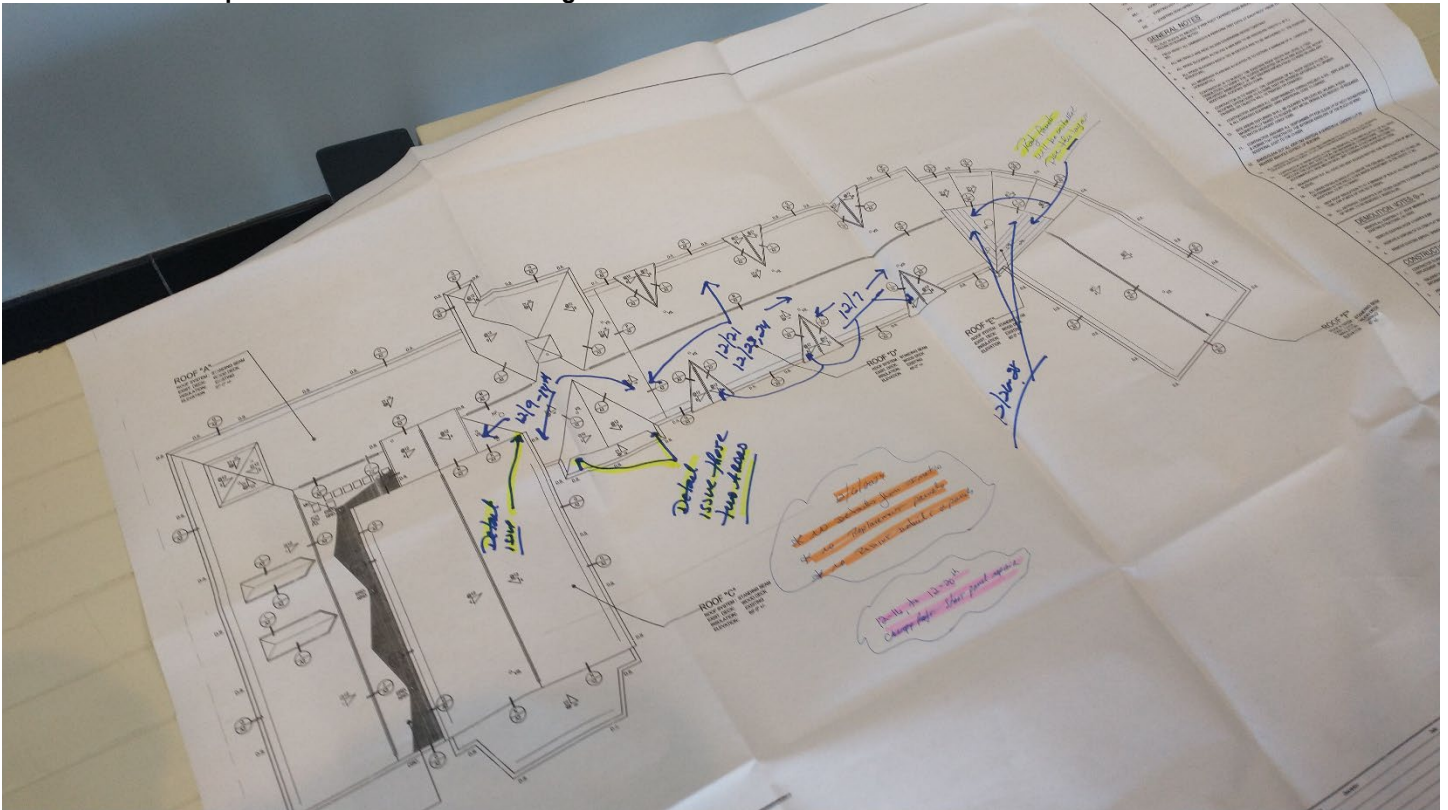

Roof plan

