



Progress Report



LEDYARD SD
4 BLONDER PARK RD
LEDYARD, CONNECTICUT 06339

FACILITY: Juliet W. Long School	ROOF SECTION: Flood and Gravel	DATE: 07/05/2024
--	---------------------------------------	-------------------------

Report Data

Report Date	07/05/2024
Title	7/5/24
Report Type	Progress Report

Gold Seal Roofing has completed the rip and base sheet installation on the roof closest to the playground. The crew was onsite Friday after the holiday to clean up the job site and move dumpsters in preparation for the continuing rip on Monday.

All field areas of the roof are looking great, with minimal rippling and great water displacement throughout.

The crew plans to start ripping the opposite side of the school on Monday (weather depending). They continue to display steady, consistent work day after day and are still aiming for a completion date around the end of July.

Thank you, and please let us know if you have any questions.

Sincerely,

Brendon Johnson

bjohnson@garlandco.com

(860)227-7946


Jeremy Cogdill

jcogdill@garlandco.com

(802)598-2974



1 Exposed decking detail on perimeter temporarily fixed- No new leaks have been observed

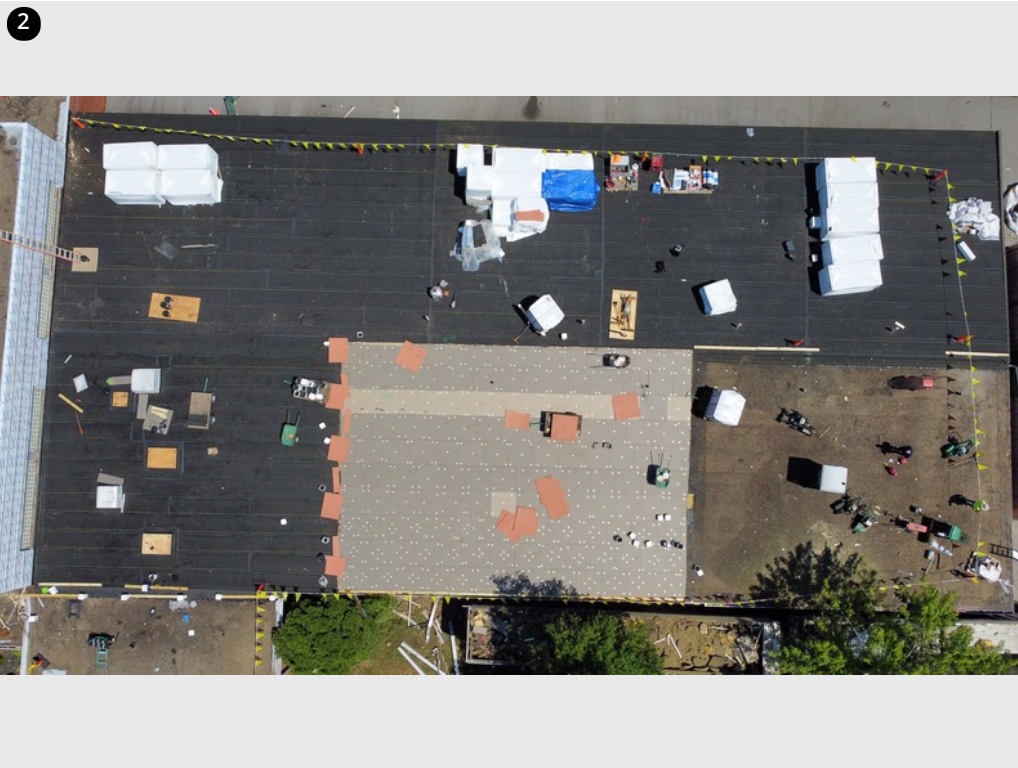

2 Overview- Progress as of 7/2



3 Overview- Fastening pattern on insulation boards



4 Crew using buckets of fasteners to weigh down adhered cover board

5



Overview- Completed base sheets on playground side

6



Masonry wall completely covered with ice and water- Hat channels installed



Overview- Crew installing base sheets on final area of playground side
