

Progress Report



FACILITY: Gales Ferry School ROOF SECTION: ALL DATE: 11/29/2024

кe	po	rt	υa	ta	

•	
Report Date	11/29/2024
Title	11/29/24
Report Type	Progress Report

Imperial was onsite Saturday installing panels on field areas located above classrooms, and were able to complete roughly 25 SQ.

The crew completed the front half of the large hip section located above the side entrance on Monday.

The weather and a holiday were a factor this week, with Tuesday being mostly a rainout, and Thursday being Thanksgiving.

Friday, the crew was working above classrooms on the playground side, completing a field area and two dormer sections.

Sincerely,

Brendon Johnson

bjohnson@garlandco.com

(860)227-7946

Jeremy Cogdill

jcogdill@garlandco.com

(802)598-2974

Panels installed Saturday 11/23/24





Panels installed Saturday 11/23/24








Panels installed Saturday 11/23/24



Fasteners observed penetrating deck-11/23/24






Overview- 11/25/24








Crew installing panels on hip section at the side entrance- 11/25/24

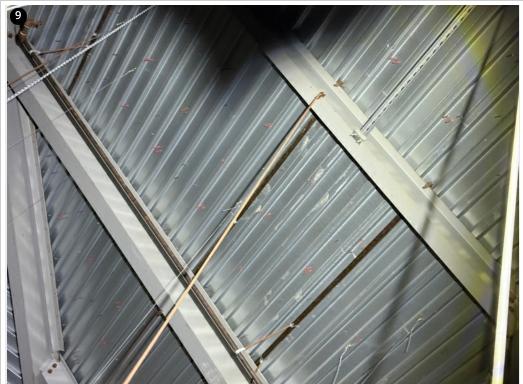

Fasteners observed penetrating deck-11/25/24

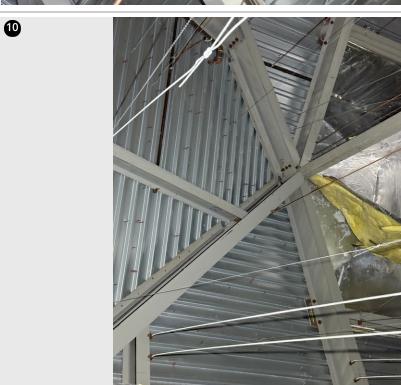

Fasteners observed penetrating deck-11/25/24









Crew installing panels on dormer-Courtyard side- 11/27/24



Crew fastening panel clips on dormer using 16" fasteners- 11/27/24



Half of dormer completed- Panels installed on field section- 11/27/24



Fasteners observed penetrating deck-11/27/24



Crew installing panels on field section-11/29/24



Crew installing panels on dormer- 11/29/24



Crew fastening clips on field section-11/27/24



Fasteners observed penetrating deck-11/29/24



Fasteners observed penetrating deck-11/29/24



Overview- 11/29/24
