



Progress Report



LEDYARD SD
4 BLONDER PARK RD
LEDYARD, CONNECTICUT 06339

FACILITY: Gales Ferry School	ROOF SECTION: ALL	DATE: 11/22/2024
-------------------------------------	--------------------------	-------------------------

Report Data

Report Date	11/22/2024
Title	11/22/24
Report Type	Progress Report

Panel installation continued this week with Imperial completing 99% of the install on the backside of the gym Tuesday. Wednesday, the crew installed temporary caps on ridges in preparation for a rain storm that came through on Thursday. No work was completed Thursday due to weather, however Imperial was onsite to investigate and address a small leak occurring in a classroom. Work resumed Friday, and the crew was able to install panels on a dormer located above the side entrance to the school.

Sincerely,

Brendon Johnson
 (860)227-7946
 bjohnson@garlandco.com

Jeremy Cogdill
 jcgdill@garlandco.com
 (802)598-2974

1

Overview- 11/18/24



2

Panels installed on backside of gym- 11/18/24





3 Fasteners observed properly penetrating deck- 11/18/24



4 Temporary caps installed on all ridges in preparation for incoming rain- 11/20/24

5



Temporary caps installed on ridge above the gym

6




Temporary caps installed on all ridge locations- 11/20/24

7



8

Temporary caps installed on all ridge locations- 11/20/24

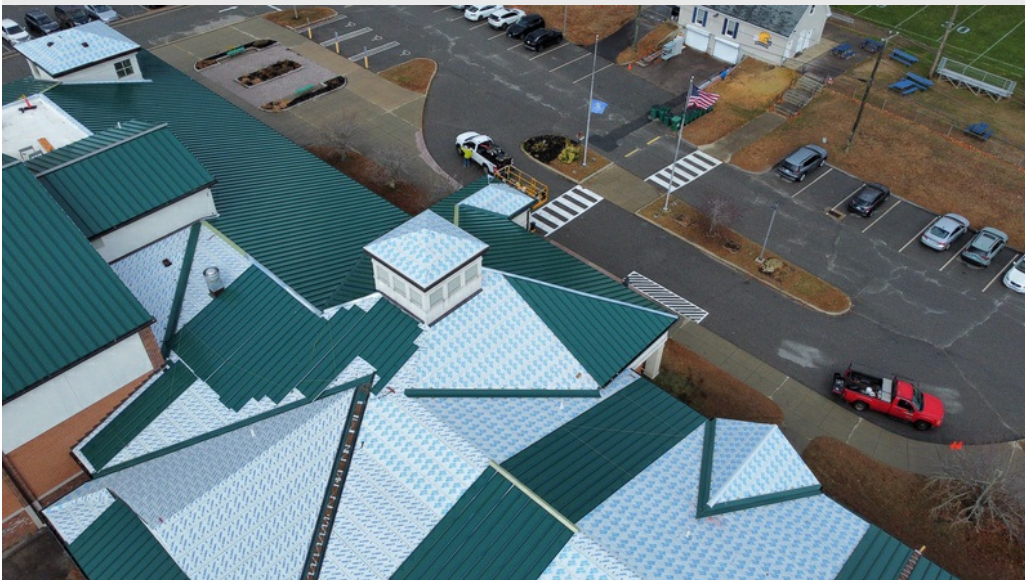

9



Temporary caps installed above kindergarten wing- 11/20/24

10



Small leak reported and addressed by Imperial near valley- 11/21/24

11

Crew installing panels on dormer above side entrance- 11/22/24



12

Crew fastening clips on dormer above side entrance- 11/22/24



13



Panels installed on dormer above side entrance-11/22/24

14



Crew taking measurements on dormer above side entrance- 11/22/24

15



Panels installed on dormer above side entrance- 11/22/24

16



Dormer above side entrance- 11/22/24

17

Overview- 11/22/24



18

Overview- 11/22/24

