



Progress Report



LEDYARD SD
4 BLONDER PARK RD
LEDYARD, CONNECTICUT 06339

FACILITY: Gales Ferry School	ROOF SECTION: ALL	DATE: 02/08/2025
------------------------------	-------------------	------------------

Report Data

Report Date	02/08/2025
Title	2/8/25
Report Type	Progress Report

Field panels on the boiler room section were installed this week in between inclement weather days.

New panels were also installed on the Kindergarten wing, and fasteners were observed penetrating the deck.

Imperial plans to be onsite this weekend. The crew is focussing on installing snow guards over all entrance and walkway areas in preparation for incoming snow storms.

Sincerely,

Brendon Johnson
bjohnson@garlandco.com
(860)227-7946

Jeremy Cogdill
jcogdill@garlandco.com
(802)598-2974

1



Overview- Boiler room section progress- 2/3/25

2



Panels installed over the weekend on Kindergarten wing- 2/3/25

3



Crew installing panels on the boiler room section- 2/4/25


4



Crew building curb around stack penetration- 2/4/25



Fasteners visible penetrating deck on Kindergarten wing- 2/4/25

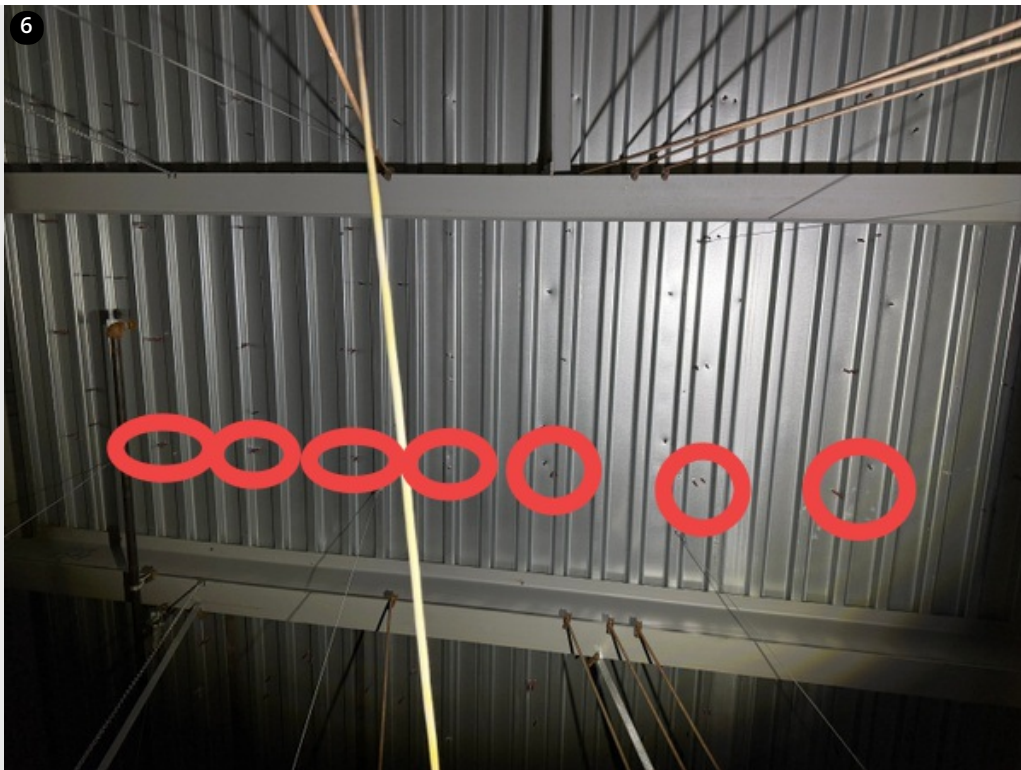

Fasteners visible penetrating deck on Kindergarten wing- 2/4/25

7

Overview- 2/5/25



8

Overview- 2/5/25



9

Overview- Boiler room section- 2/5/25



10

Crew riveting panel ends on boiler room section- 2/7/25



11



Crew riveting panel ends over Kindergarten wing- 2/7/25
