



Field Report No.:		04			
SP&A Project No: 22.331		Report Date: 08-02-2024	Time: 9:30AM		
Project: Juliet Long School (Name & Location) 1854 CT-12 Gales Ferry, CT 06335 General Contractor: Gold Seal Roofing, LLC					
Weather		Site Conditions		Day of Week	
<input type="checkbox"/> Temp. Range: 79° <input checked="" type="checkbox"/> Clear <input type="checkbox"/> Rain <input type="checkbox"/> Foggy <input type="checkbox"/> Warm <input type="checkbox"/> Overcast <input type="checkbox"/> Snow <input type="checkbox"/> Cold <input type="checkbox"/> Hot		<input checked="" type="checkbox"/> Clear <input type="checkbox"/> Dusty <input type="checkbox"/> Muddy <input type="checkbox"/> Windy <input type="checkbox"/> Other		<input type="checkbox"/> Monday <input type="checkbox"/> Thursday <input type="checkbox"/> Tuesday <input checked="" type="checkbox"/> Friday <input type="checkbox"/> Wednesday <input type="checkbox"/> Saturday	
Type of Work Observed Being Performed					
1	<input type="checkbox"/> Site work	7	<input type="checkbox"/> General Trades/Drywall	13	<input type="checkbox"/> Specialties/ Food Service
2	<input type="checkbox"/> Demolition	8	<input type="checkbox"/> Windows & Doors	14	<input type="checkbox"/> Elevators
3	<input type="checkbox"/> Concrete	9	<input checked="" type="checkbox"/> Roofing	15	<input type="checkbox"/> Plumbing
4	<input type="checkbox"/> Masonry	10	<input type="checkbox"/> Flooring	16	<input type="checkbox"/> HVAC
5	<input type="checkbox"/> Steel/Misc. Metals	11	<input type="checkbox"/> Pool	17	<input type="checkbox"/> Electrical
6	<input type="checkbox"/> Carpentry/Casework/ Mill Work	12	<input type="checkbox"/> Painting/Interior Finishes	18	<input type="checkbox"/> Temperature Controls/BMS
19	<input type="checkbox"/> Sprinkler	20	<input checked="" type="checkbox"/> Finish metal	21	<input type="checkbox"/> Iron workers
		22	<input type="checkbox"/> Tester (Tri-state)	23	<input type="checkbox"/> Audio Vis/Low Volt
		24	<input type="checkbox"/> Other:		
Work Performed at time of site visit:					
<ul style="list-style-type: none"> - Approximate number of workers on site – 10 - Working on installing insulation boards on roof B. - Working on installing the metal trim above the windows - Working on general site clean - Installation of the electrical line work is in progress. See attached photo. 					
General Remarks:					
<ul style="list-style-type: none"> - Project is on schedule. - Half of roof B insulation panels are installed at the time of the site visit. The second half will be installed the tomorrow (8/3) as well as the base cap for water issues over the weekend. - The roof drain line has been corrected. The original line was not connected to any pipes and had ended below ground into the soil. See attached photo. 					
Visitors:					
- None.					
Construction Administrator:		Steven June		8/05/2024	
		<i>(Print Name)</i>		<i>(Signature)</i>	
Copies To:		<input type="checkbox"/> CA <input type="checkbox"/> Architect <input checked="" type="checkbox"/> Contractor <input checked="" type="checkbox"/> Owners			

PHOTOS (see next page);

Roof edge trim being installed



Roof B installation of the insulation panels




Roof B installation of the insulation panels



Roof B installation of the insulation panels. Area to the right is to be replaced the following day.



Roof B – PT board for raising of the parapet since the roof pitch was not discovered until the roofing material was removed

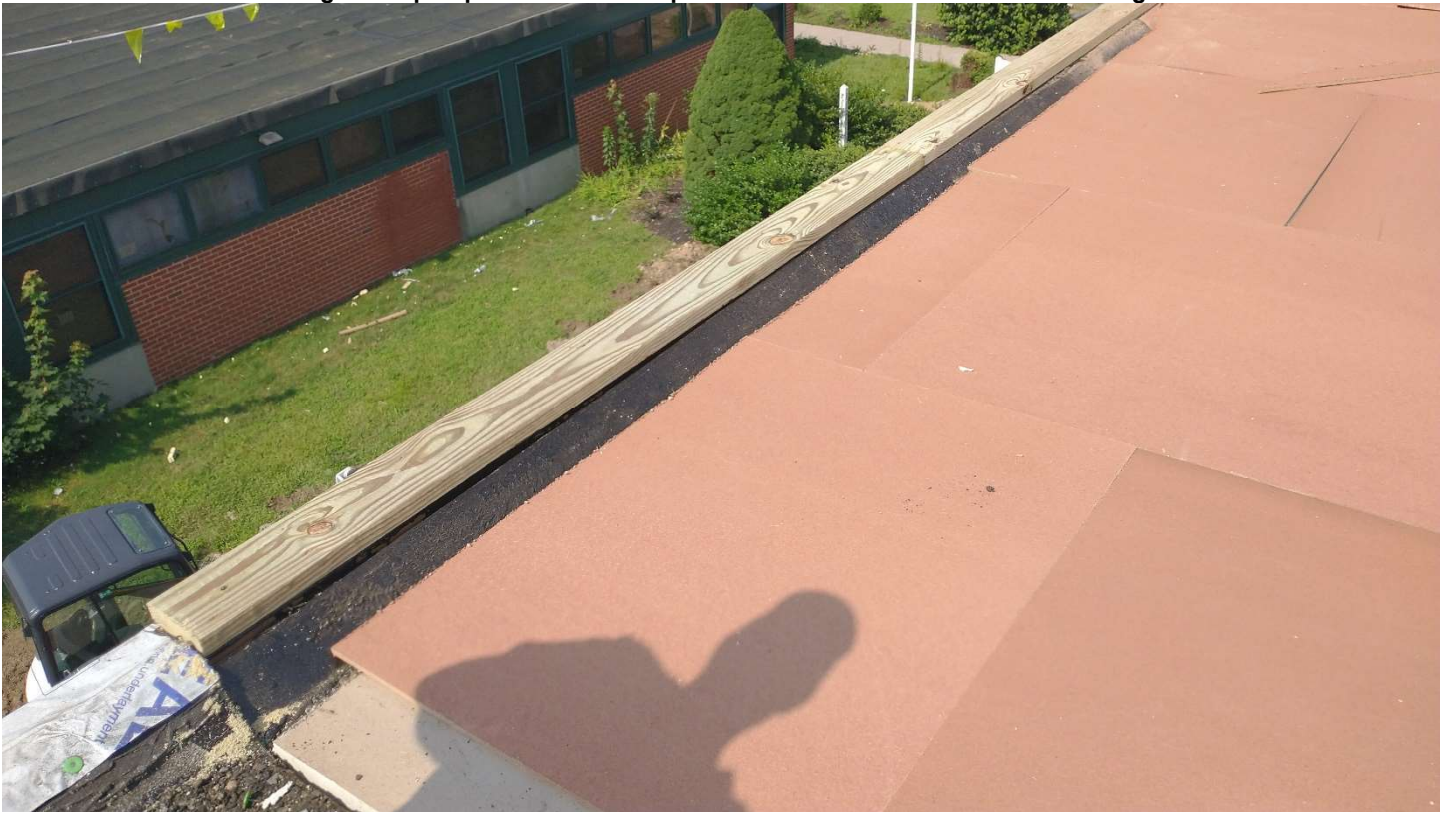

Roof E – PT boards installed for kick out of the new metal panels



Electrical trench work in progress



Roof drainage line corrected and needs to be backfilled



Roof plan

