



Progress Report



LEDYARD SD
4 BLONDER PARK RD
LEDYARD, CONNECTICUT 06339

FACILITY: Board of Education Building	ROOF SECTION: Board Of Ed Roof	DATE: 11/29/2024
--	---------------------------------------	-------------------------

Report Data

Report Date	11/29/2024
Title	11/29/24
Report Type	Progress Report

As of Friday 11/29, the South, West and North roof sections have been completed.

Tuesday and Thursday were off days due to the weather and the Thanksgiving holiday.

Friday the crew was working on the East sloped section.

The crew plans to be back onsite Saturday to continue progress.

Sincerely,

Brendon Johnson

bjohnson@garlandco.com

(860)227-7946

Jeremy Cogdill

jcogdill@garlandco.com


(802)598-2974




Crew installing panels on West side-
11/25/24



Clips fastened 11/25/24

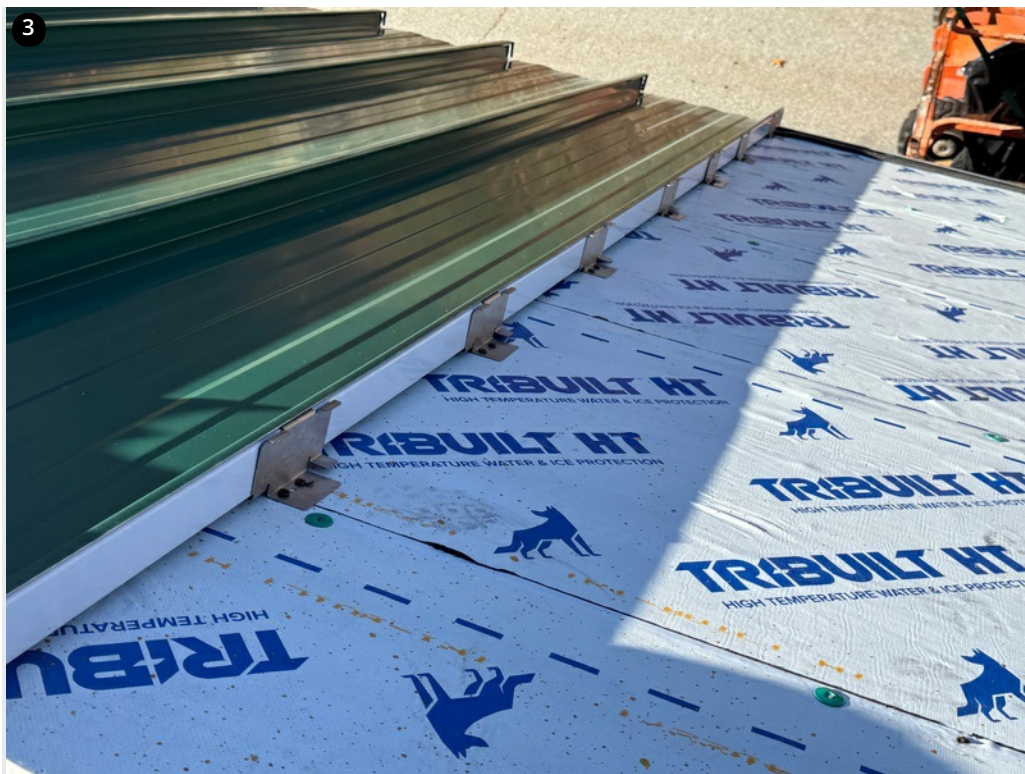

Overview- Clip spacing

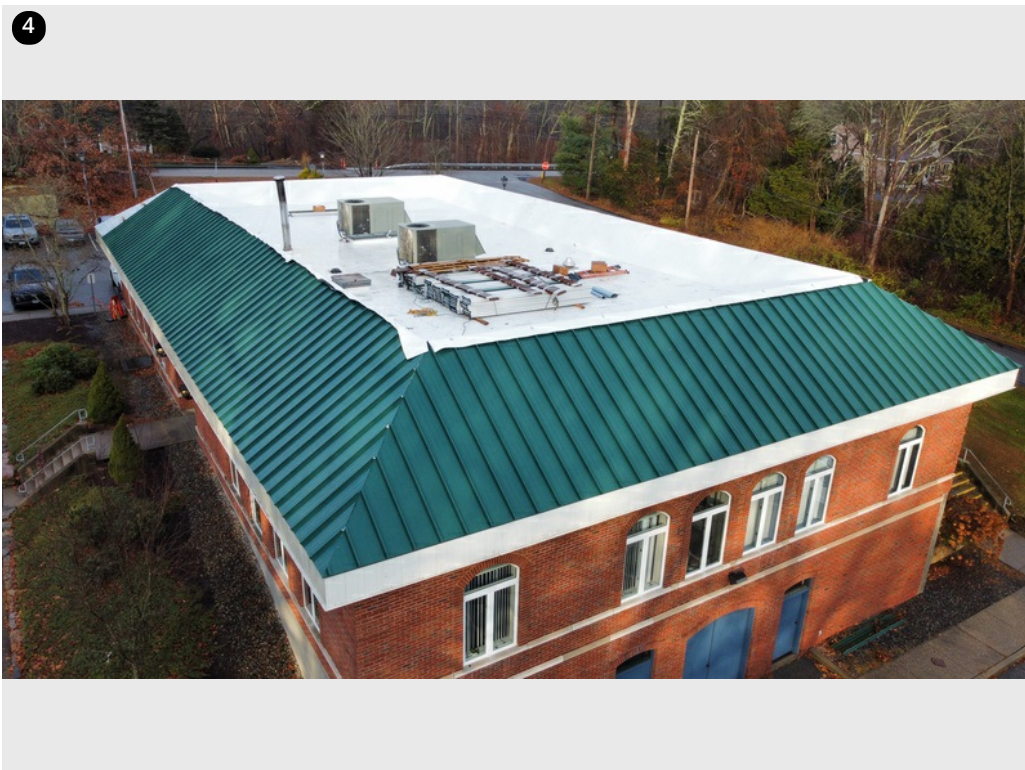

Overview- 11/26/24

5

Panels staged for install- 11/26/24




6

Overview- 11/26/24



7

Overview- 11/26/24

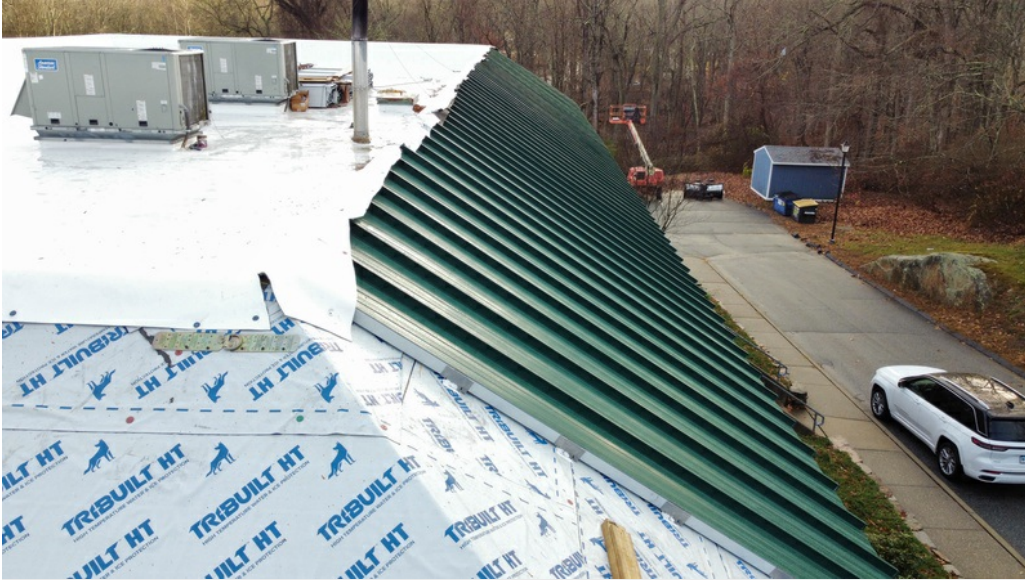

8

Overview- 11/26/24



9



Crew fastening clips on North side
11/27/24

10



Overview-11/27/24



Crew installing panels on North East corner- 11/27/24



Crew riveting panel ends- 11/29/24



Clips installed 11/29/24



Overview- North side completed
