



# Progress Report



LEDYARD SD  
4 BLONDER PARK RD  
LEDYARD, CONNECTICUT 06339

<b>FACILITY:</b> Juliet W. Long School	<b>ROOF SECTION:</b> Flood and Gravel	<b>DATE:</b> 07/19/2024
--	---------------------------------------	-------------------------

## Report Data

<b>Report Date</b>	07/19/2024
<b>Title</b>	7/19/24
<b>Report Type</b>	Progress Report

The crew from Gold Seal Roofing ripped another section of roughly 20-25 SQ on Friday, leaving just one more similar sized area left to go on that wing.

Gold Seal continues to do a great job with base sheet installation. Proper adhesive coverage rates are being applied on field sheets, with good consistent bleed out on lap seams. All perimeter blocking is being covered completely with base sheets or an ice and water layer. Cant strips are being added to all curb flashings and all flashings are being adhered well with no open conditions observed.

The plan is to jump to the connector roof on Monday, to coordinate with scheduled drain plumbing work starting inside the school that day.

Sincerely,

**Brendon Johnson**

[bjohnson@garlandco.com](mailto:bjohnson@garlandco.com)

(860)227-7946

**Jeremy Cogdill**

[jcogdill@garlandco.com](mailto:jcogdill@garlandco.com)

(802)598-2974

1

Overview-7/15




2

Overview-7/16



3

Overview-7/18

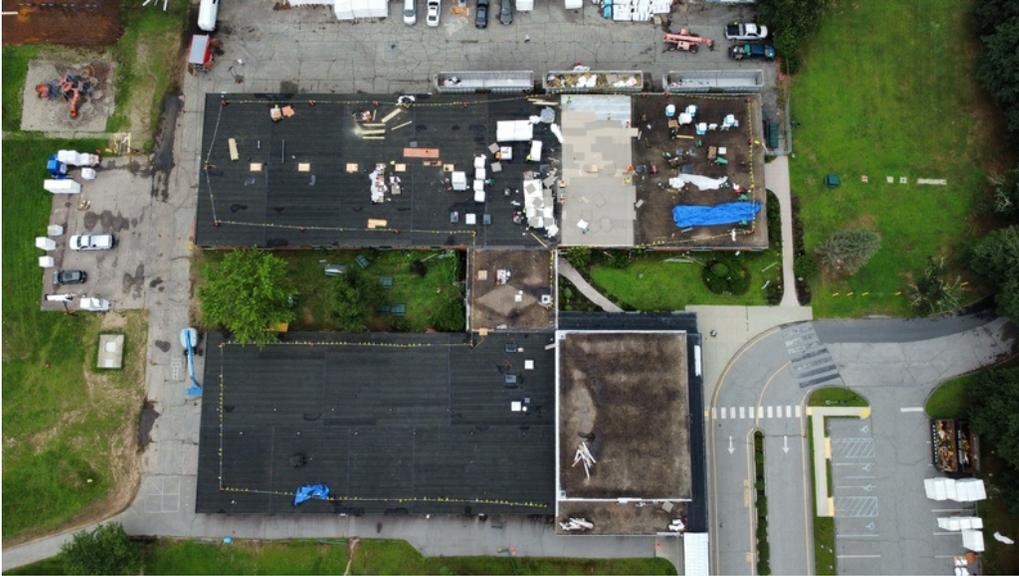

4

Perimeter blocking covered with base sheets and back nailed





5

Good bleed out- No open seams



6

Hoods were removed to accommodate new system height- Openings are being temporarily covered with EPDM-Cant strips will be put in place around curbs



7 Chimney with completed ice and water application- Hat channels are secured- Base flashings completed with cant strips in place



8 Base flashings around chimney- Proper height- No open corners or seams



9 Fascia blocking has been installed around the perimeter-Will be covered with ice and water



10 Field- Good bleed out at lap seams- Sheets lapped correctly for slope- Fascia blocking installed

