



<b>Field Report No.:</b>		<b>07</b>	
<b>SP&amp;A Project No:</b> 22.331		<b>Report Date:</b> 08-23-2024	
<b>Project:</b> Juliet Long School (Name & Location) 1854 CT-12 Gales Ferry, CT 06335		<b>Time:</b> 9:30AM	
<b>General Contractor:</b> Gold Seal Roofing, LLC			
<b>Weather</b>		<b>Site Conditions</b>	
<input type="checkbox"/> Temp. Range: 78° <input checked="" type="checkbox"/> Clear <input type="checkbox"/> Rain <input type="checkbox"/> Foggy <input type="checkbox"/> Warm <input type="checkbox"/> Overcast <input type="checkbox"/> Snow <input type="checkbox"/> Cold <input type="checkbox"/> Hot		<input checked="" type="checkbox"/> Clear <input type="checkbox"/> Dusty <input type="checkbox"/> Muddy <input type="checkbox"/> Windy <input type="checkbox"/> Other	
<b>Day of Week</b>			
<input type="checkbox"/> Monday <input type="checkbox"/> Thursday <input type="checkbox"/> Tuesday <input checked="" type="checkbox"/> Friday <input type="checkbox"/> Wednesday <input type="checkbox"/> Saturday			
<b>Type of Work Observed Being Performed</b>			
1	<input type="checkbox"/> Site work	7	<input type="checkbox"/> General Trades/Drywall
2	<input type="checkbox"/> Demolition	8	<input type="checkbox"/> Windows & Doors
3	<input type="checkbox"/> Concrete	9	<input checked="" type="checkbox"/> Roofing
4	<input type="checkbox"/> Masonry	10	<input type="checkbox"/> Flooring
5	<input type="checkbox"/> Steel/Misc. Metals	11	<input type="checkbox"/> Pool
6	<input type="checkbox"/> Carpentry/Casework/ Mill Work	12	<input type="checkbox"/> Painting/Interior Finishes
13	<input type="checkbox"/> Specialties/ Food Service	14	<input type="checkbox"/> Elevators
15	<input type="checkbox"/> Plumbing	16	<input type="checkbox"/> HVAC
17	<input type="checkbox"/> Electrical	18	<input type="checkbox"/> Temperature Controls/BMS
19	<input type="checkbox"/> Sprinkler	20	<input checked="" type="checkbox"/> Finish metal
		21	<input type="checkbox"/> Iron workers
		22	<input type="checkbox"/> Tester (Tri-state)
		23	<input type="checkbox"/> Audio Vis/Low Volt
		24	<input type="checkbox"/> Other:
<b>Work Performed at time of site visit:</b>			
<ul style="list-style-type: none"> <li>- Approximate number of workers on site – 8</li> <li>- Installing the skylights. See note below. See attached photo.</li> <li>- Working on the small parapets on roof A. See attached photo.</li> <li>- Working detail work for roof D. See attached photo.</li> <li>- One individual was removing the plastic wrap on the panels.</li> <li>- General cleaning was in progress.</li> </ul>			
<b>General Remarks:</b>			
<ul style="list-style-type: none"> <li>- Project is on schedule.</li> <li>- Panels for the walls of roof B are on site. Panel work to start week of 8/26. See attached photo.</li> <li>- While on site, the observer noticed that the security bars for the skylights looked like a primer grey. After further research, the specifications call for the bars to be white</li> </ul>			
<b>Visitors:</b>			
- None.			
<b>Construction Administrator:</b> Steven June		<b>8/26/2024</b>	
<small>(Print Name)</small>		<small>(Signature)</small>	
		<small>(Date)</small>	
<b>Copies To:</b>	<input type="checkbox"/> CA	<input type="checkbox"/> Architect	<input checked="" type="checkbox"/> Contractor <input checked="" type="checkbox"/> Owners

PHOTOS (see next page);

**Roof A – Parapet work**




**Detail work on roof D**





Skylight area work in progress. Safety bars need to be white as per the specifications.

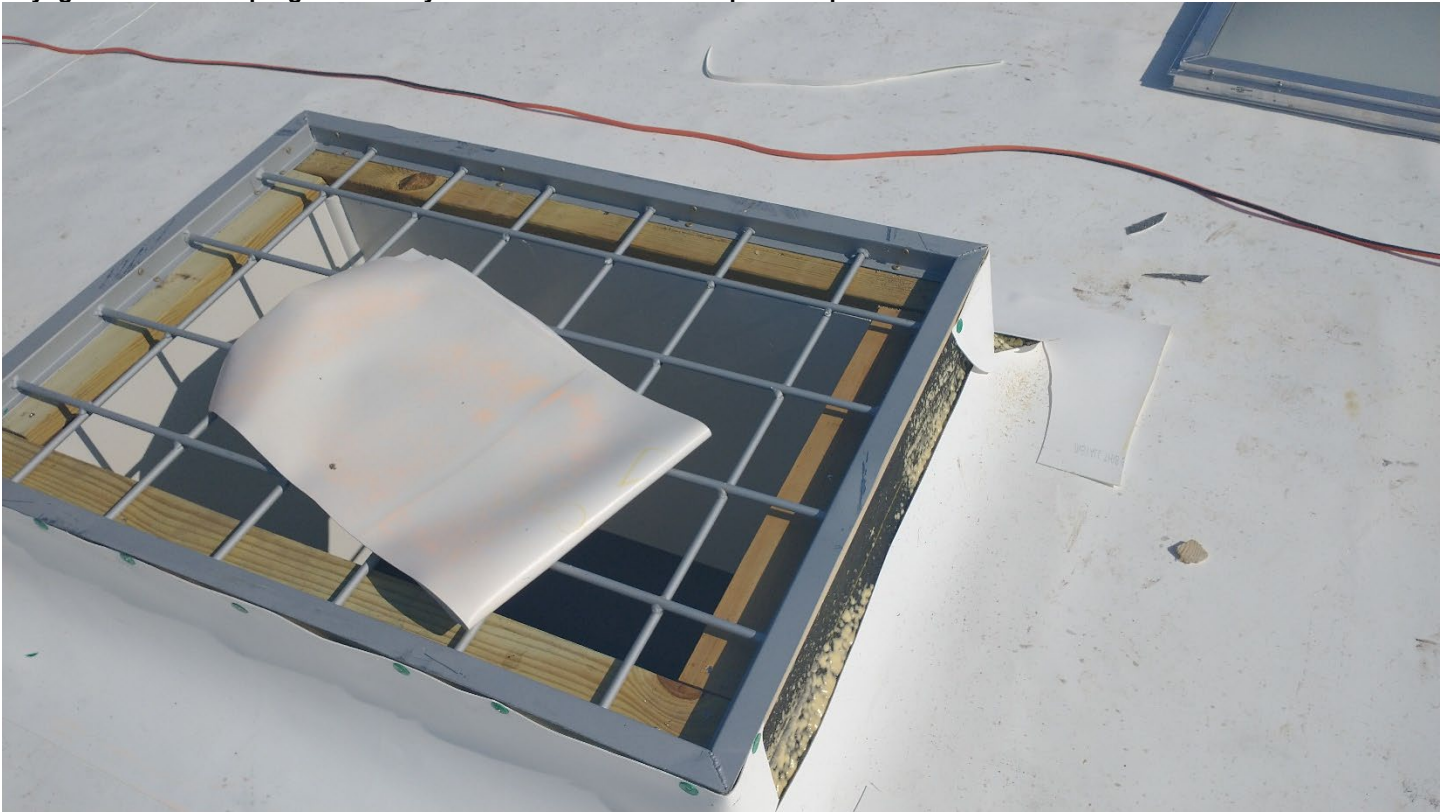

Roof A work in progress





**Panels ready to be installed**



**Roof A – Soil vent work**



**Roof plan**

