



# Progress Report



LEDYARD SD  
4 BLONDER PARK RD  
LEDYARD, CONNECTICUT 06339

FACILITY: Gales Ferry School	ROOF SECTION: ALL	DATE: 02/21/2025
------------------------------	-------------------	------------------

## Report Data

Report Date	02/21/2025
Title	2/21/25
Report Type	Progress Report

On Wednesday, the crew was installing head enclosures on the front section of the school near the bus loading/dropoff zone. Crews were also working on fastener replacement on the kindergarten wing and finished the majority of the replacements on Saturday. Note: "8" fasteners will switch to black due to a lack of red fastener availability"

The week ahead looks good weatherwise which means crews will continue on trim work and fastener replacement on the gym section.

Sincerely,

Brendon Johnson - [bjohnson@garlandco.com](mailto:bjohnson@garlandco.com) - (860)227-7946

Jeremy Cogdill - [jcogdill@garlandco.com](mailto:jcogdill@garlandco.com) - (802)598-2974




Working on the low slope to slope head detail

2



Overview of the blocking wrapped

3

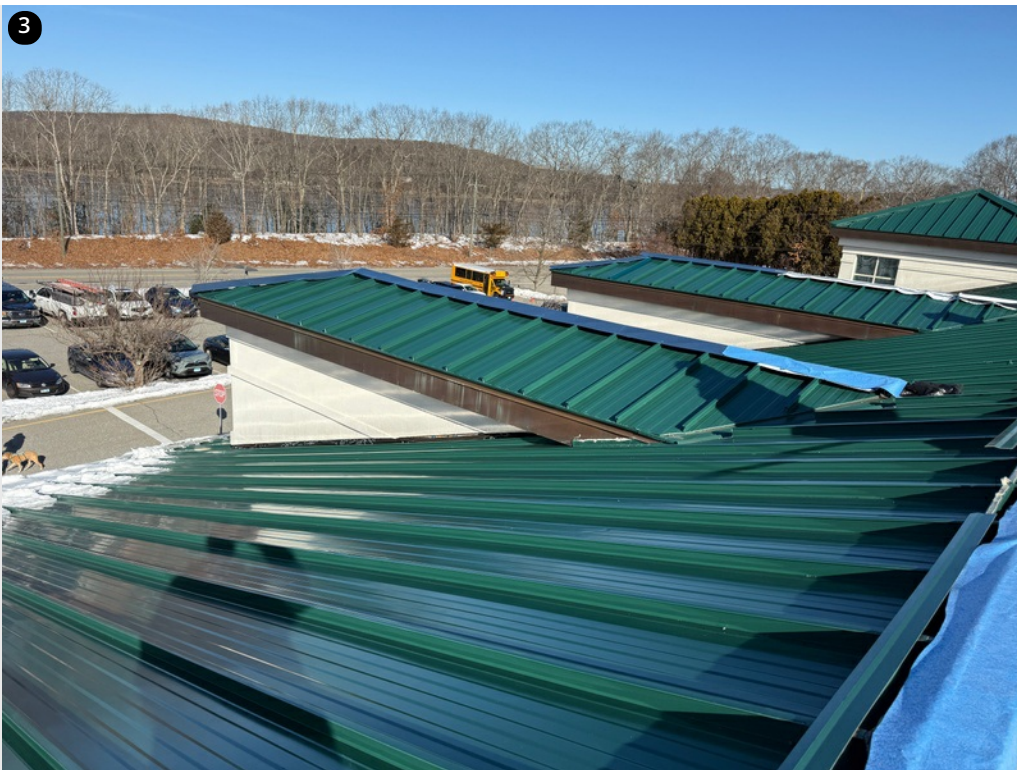

Ridge cap install



4



Wrapping closure piece

5



Crew starting fastener replacement on the back of the kindergartener wing

6



Verification of clip spacing and 7" fasteners existing, the crew is installing 8"

7



Overview of completed fascia on dormers



8



Crew on the back side of the kindergarten wing

9



Replacing fasteners with 8" HD's



Verification of 8" fasteners and clip spacing



Proper deck fastening pattern with 8" fasteners



12



Overview of the kindergarten wing completed fastener replacement

13



Area of detail question with the SD

14



Due to existing cop flashing, the question of what to do here and what color is outstanding.

15



Verification of fasteners utilized - 8" HD
