



Field Report No.:		14	
SP&A Project No: 22.331		Report Date: 11-22-2024	Time: 9:30AM
Project: Gales Ferry School (Name & Location) 1854 CT-12 Gales Ferry, CT 06335		General Contractor: The Imperial Company, Inc.	
Weather		Site Conditions	
<input type="checkbox"/> Temp. Range: 53° <input type="checkbox"/> Clear <input checked="" type="checkbox"/> Rain <input type="checkbox"/> Foggy <input type="checkbox"/> Warm <input checked="" type="checkbox"/> Overcast <input type="checkbox"/> Snow <input type="checkbox"/> Cold <input type="checkbox"/> Hot		<input checked="" type="checkbox"/> Clear <input type="checkbox"/> Dusty <input type="checkbox"/> Muddy <input type="checkbox"/> Windy <input type="checkbox"/> Other	
Day of Week			
<input type="checkbox"/> Monday		<input type="checkbox"/> Thursday	
<input type="checkbox"/> Tuesday		<input checked="" type="checkbox"/> Friday	
<input type="checkbox"/> Wednesday		<input type="checkbox"/> Saturday	
Type of Work Observed Being Performed			
1	<input type="checkbox"/> Site work	7	<input type="checkbox"/> General Trades/Drywall
2	<input type="checkbox"/> Demolition	8	<input type="checkbox"/> Windows & Doors
3	<input type="checkbox"/> Concrete	9	<input type="checkbox"/> Roofing
4	<input type="checkbox"/> Masonry	10	<input type="checkbox"/> Flooring
5	<input type="checkbox"/> Steel/Misc. Metals	11	<input type="checkbox"/> Pool
6	<input type="checkbox"/> Carpentry/Casework/ Mill Work	12	<input type="checkbox"/> Painting/Interior Finishes
13	<input type="checkbox"/> Specialties/ Food Service	14	<input type="checkbox"/> Elevators
15	<input type="checkbox"/> Plumbing	16	<input type="checkbox"/> HVAC
17	<input type="checkbox"/> Electrical	18	<input type="checkbox"/> Temperature Controls/BMS
19	<input type="checkbox"/> Sprinkler	20	<input checked="" type="checkbox"/> Finish metal
21	<input type="checkbox"/> Iron workers	22	<input type="checkbox"/> Tester (Tri-state)
23	<input type="checkbox"/> Audio Vis/Low Volt	24	<input type="checkbox"/> Other:
Work Performed at time of site visit:			
- Approximate number of workers on site – 2 - Installing panels on the north side of roof A, to the left of the main entrance. Working on the ridge area. See attached photo.			
General Remarks:			
- Crew will be working on Saturday (11/23). - Work is to continue working east on the north roof A. - Imperial still needs to remove the short screws & install new 8” screws in the selected area from 11/11’s site meeting. - School will be closed next week from Wednesday to Friday (11/27-29)			
Visitors:			
- None.			
Construction Administrator: Steven June		11/22/2024	
<i>(Print Name)</i>		<i>(Signature)</i>	
<i>(Date)</i>			
Copies To:	<input type="checkbox"/> CA	<input type="checkbox"/> Architect	<input checked="" type="checkbox"/> Contractor <input checked="" type="checkbox"/> Owners

PHOTOS (see attached photos);


Roof A – North elevation work at time of site visit



Roof A – temporary ridge caps



Roof A – Waiting for rake trim

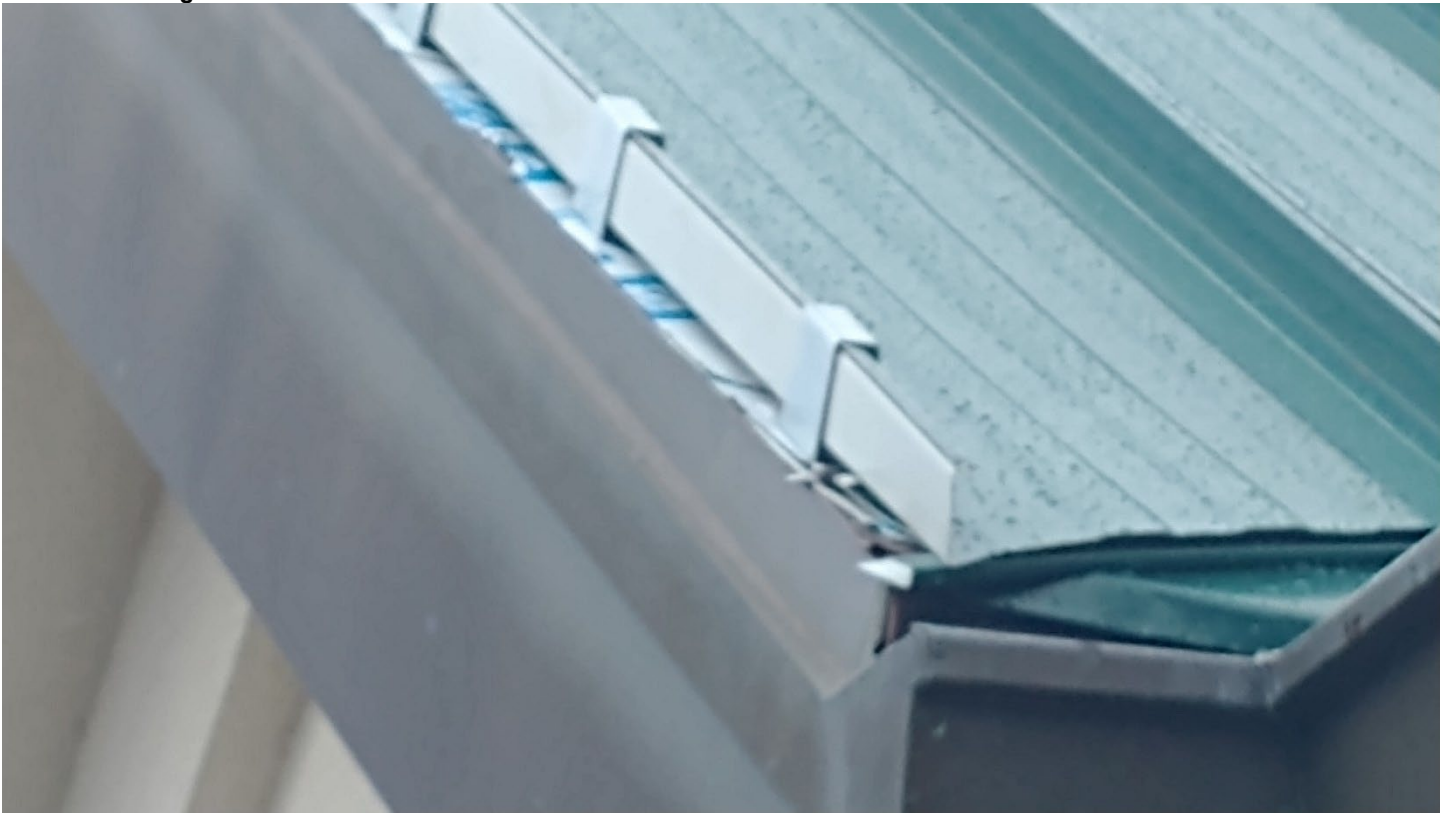

Roof plan

