



Progress Report



LEDYARD SD
4 BLONDER PARK RD
LEDYARD, CONNECTICUT 06339

FACILITY: Board of Education Building	ROOF SECTION: Board Of Ed Roof	DATE: 11/22/2024
----------------------------------------------	---------------------------------------	-------------------------

Report Data

Report Date	11/22/2024
Title	11/22/24
Report Type	Progress Report

Imperial began metal panel installation this week at the BOE building.
 Materials were loaded to the roof and prepped on Monday. All clips are to be spaced at 1'8" throughout the entire roof.
 Thursday was a rainout, but the crew was able to complete the majority of the back section when they returned on Friday.


Sincerely,

Brendon Johnson
 (860)227-7946
 bjohnson@garlandco.com

Jeremy Cogdill
 (802)598-2974
 jcogdill@garlandco.com



Panels loaded onto roof and prepped for installation- 11/18/24

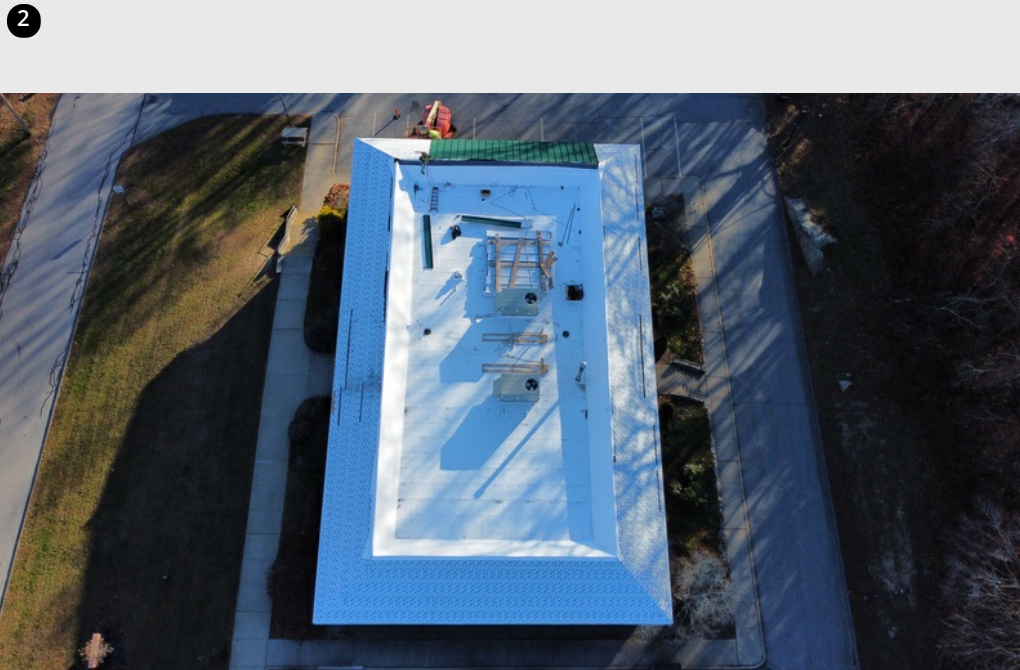

Crew installing panels on back section- 11/19/24

3

Crew installing panels on back section-
11/19/24



4

Crew installing panels on back section-
11/19/24



5



Clips fastened and spaced at 1' 8" throughout- 11/19/24

6



Crew installing panels on back section- 11/19/24

7



Crew installing panels on back section-
11/22/24

8



Panels are straight and free of camber-
11/22/24

9



Crew installing panels on back section-
11/22/24

10



Overview- 11/22/24

11

Overview- 11/22/24



12

Crew fastening clips on back section-
11/22/24

