



# Progress Report



LEDYARD SD  
4 BLONDER PARK RD  
LEDYARD, CONNECTICUT 06339

<b>FACILITY:</b> Gales Ferry School	<b>ROOF SECTION:</b> ALL	<b>DATE:</b> 02/08/2025
-------------------------------------	--------------------------	-------------------------

## Report Data

<b>Report Date</b>	02/08/2025
<b>Title</b>	2/8/25
<b>Report Type</b>	Progress Report

Field panels on the boiler room section were installed this week in between inclement weather days.

New panels were also installed on the Kindergarten wing, and fasteners were observed penetrating the deck.

Imperial plans to be onsite this weekend. The crew is focussing on installing snow guards over all entrance and walkway areas in preparation for incoming snow storms.

Sincerely,

Brendon Johnson  
 bjohnson@garlandco.com  
 (860)227-7946

Jeremy Cogdill  
 jcogdill@garlandco.com  
 (802)598-2974



1 Overview- Boiler room section progress- 2/3/25



2 Panels installed over the weekend on Kindergarten wing- 2/3/25

3




Crew installing panels on the boiler room section- 2/4/25

4




Crew building curb around stack penetration- 2/4/25



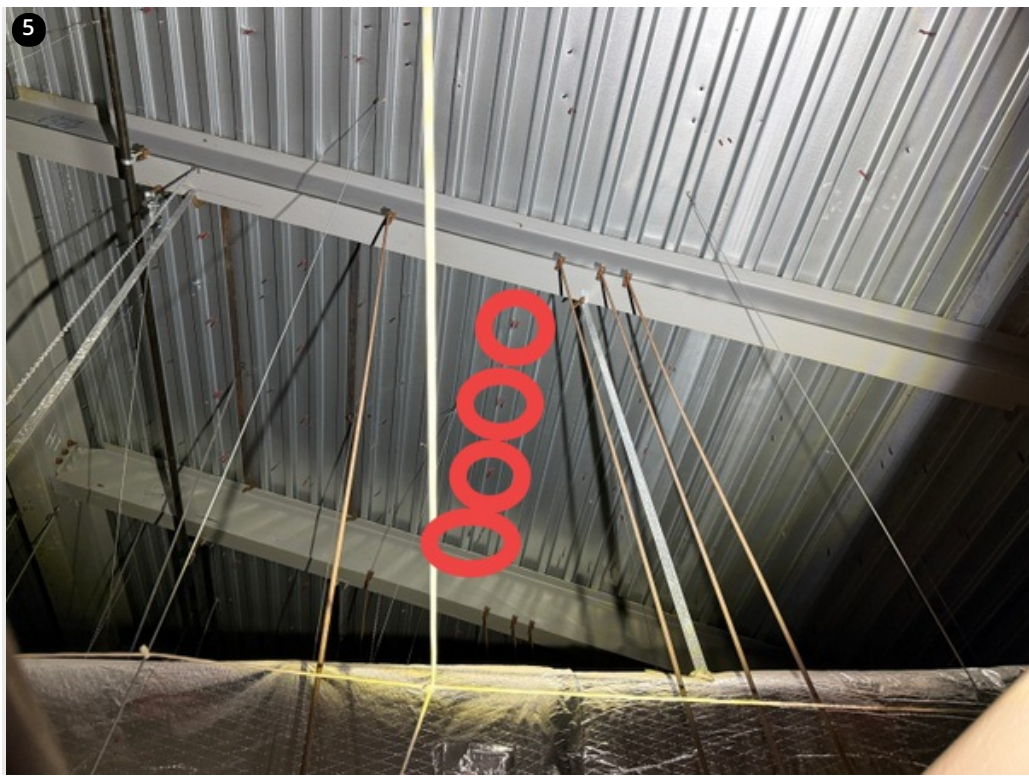

Fasteners visible penetrating deck on Kindergarten wing- 2/4/25

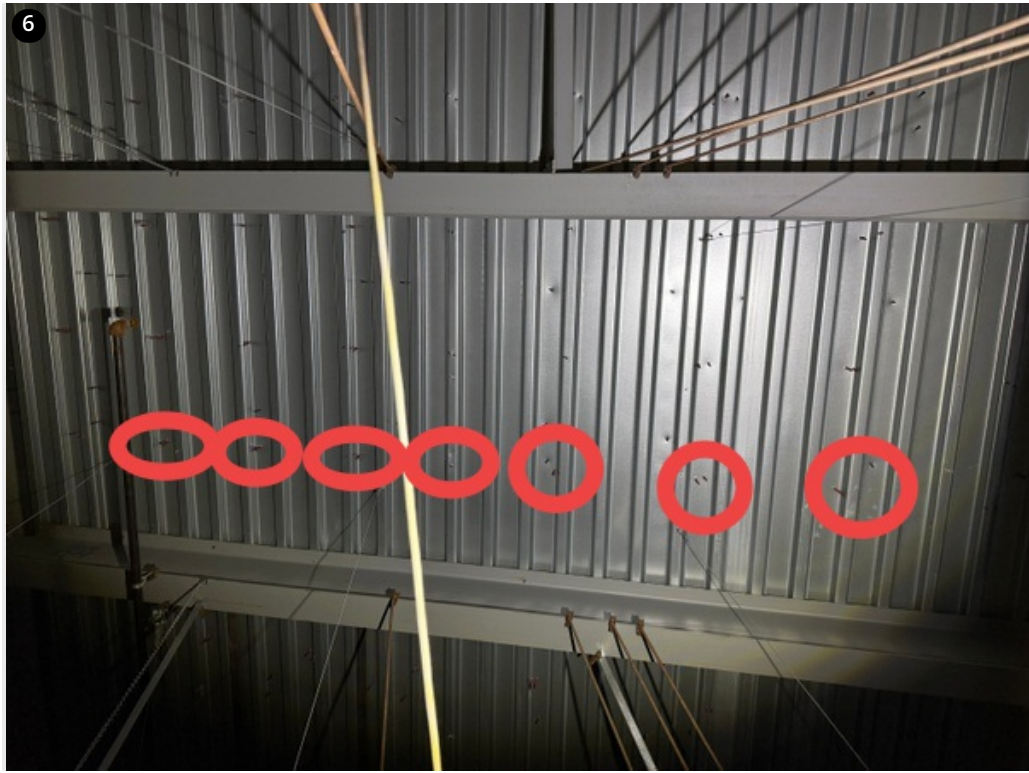

Fasteners visible penetrating deck on Kindergarten wing- 2/4/25

7

Overview- 2/5/25



8

Overview- 2/5/25





9

Overview- Boiler room section- 2/5/25



10

Crew riveting panel ends on boiler room section- 2/7/25



11



Crew riveting panel ends over Kindergarten wing- 2/7/25
