



# Progress Report



LEDYARD SD  
4 BLONDER PARK RD  
LEDYARD, CONNECTICUT 06339

<b>FACILITY:</b> Board of Education Building	<b>ROOF SECTION:</b> Board Of Ed Roof	<b>DATE:</b> 11/29/2024
--	---------------------------------------	-------------------------

## Report Data

<b>Report Date</b>	11/29/2024
<b>Title</b>	11/29/24
<b>Report Type</b>	Progress Report

As of Friday 11/29, the South, West and North roof sections have been completed.

Tuesday and Thursday were off days due to the weather and the Thanksgiving holiday.

Friday the crew was working on the East sloped section.

The crew plans to be back onsite Saturday to continue progress.

Sincerely,

**Brendon Johnson**

[bjohnson@garlandco.com](mailto:bjohnson@garlandco.com)

(860)227-7946

**Jeremy Cogdill**

[jcogdill@garlandco.com](mailto:jcogdill@garlandco.com)


(802)598-2974




Crew installing panels on West side-  
11/25/24



Clips fastened 11/25/24

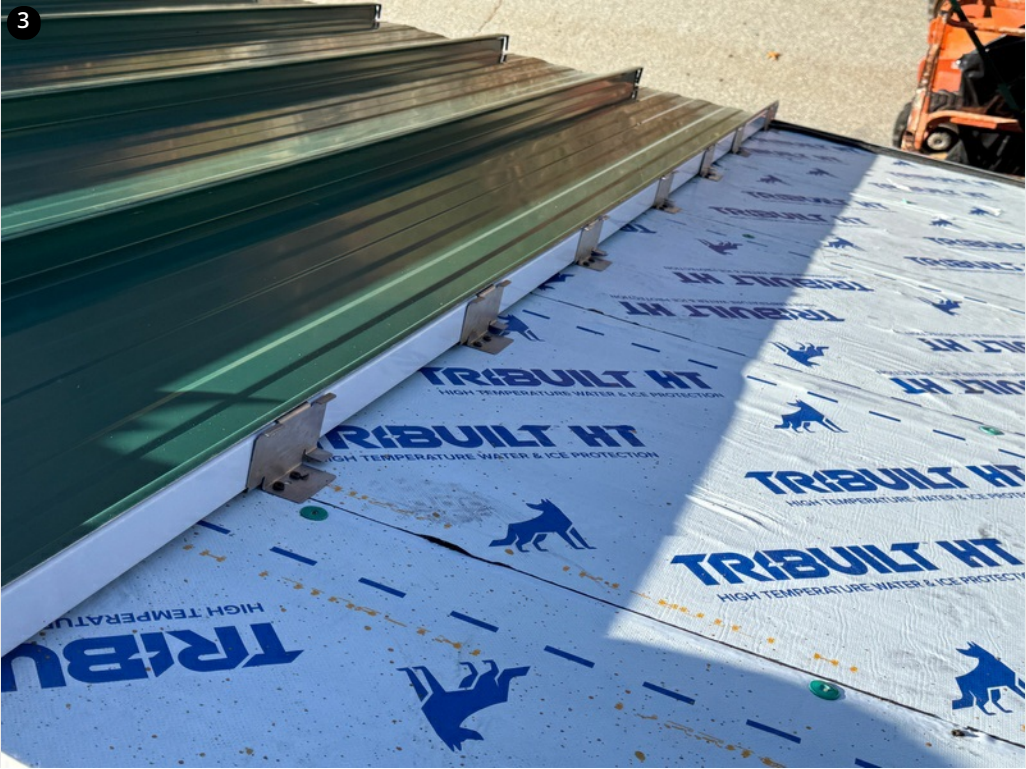

Overview- Clip spacing

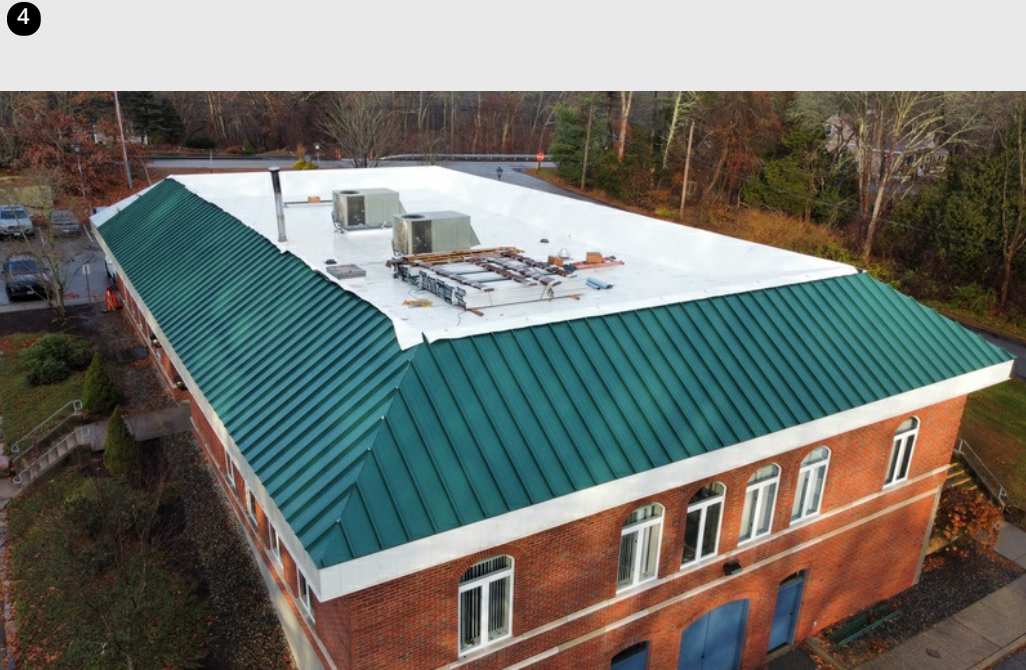

Overview- 11/26/24



5

Panels staged for install- 11/26/24




6

Overview- 11/26/24



7

Overview- 11/26/24

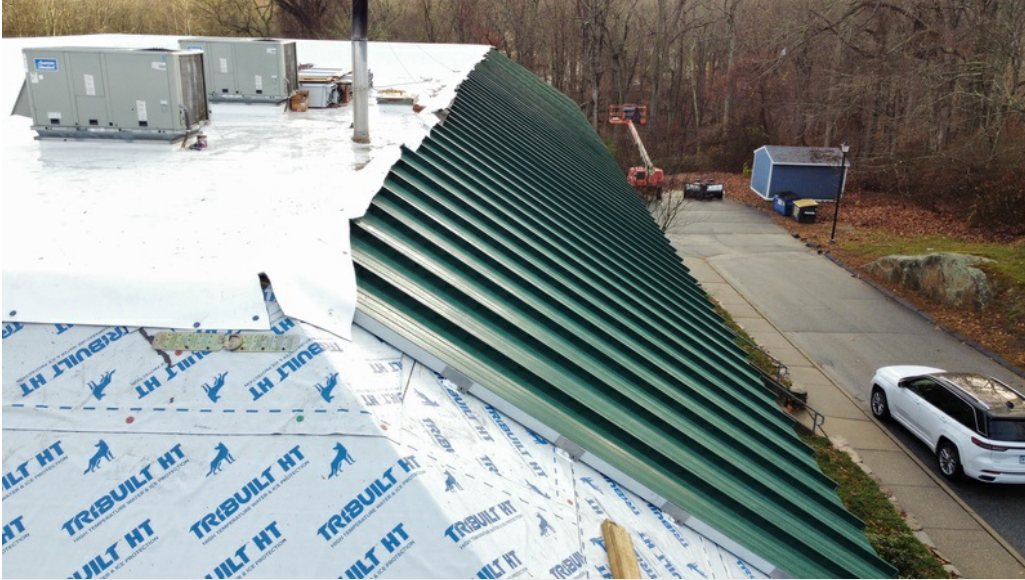

8

Overview- 11/26/24





9



Crew fastening clips on North side  
11/27/24

10



Overview-11/27/24



Crew installing panels on North East corner- 11/27/24



Crew riveting panel ends- 11/29/24





Clips installed 11/29/24



Overview- North side completed
