



Progress Report



LEDYARD SD
4 BLONDER PARK RD
LEDYARD, CONNECTICUT 06339

FACILITY: Gales Ferry School	ROOF SECTION: ALL	DATE: 12/06/2024
-------------------------------------	--------------------------	-------------------------

Report Data

Report Date	12/06/2024
Title	12/6/24
Report Type	Progress Report

Panels were installed on classroom areas on Saturday, as well as a number of dormers located on the back side of the school. Throughout the week, the crew from imperial completed installation on dormers, and worked on field areas not directly located above classrooms.

No work was completed on Thursday due to inclement weather, but Imperial was onsite to address a few leaks reported in classrooms.

The walkway roof was started on Wednesday and continued Friday.

The crew plans to be back onsite Saturday, to continue work above classroom areas not accessible during school hours.

Sincerely,

Brendon Johnson
 (860)227-7946
 bjohnson@garlandco.com

Jeremy Cogdill
 (802)598-2974
 jcogdill@garlandco.com




Panels installed on field areas and dormer- Saturday 11/30/24



Panels installed on dormer- 11/30/24

3

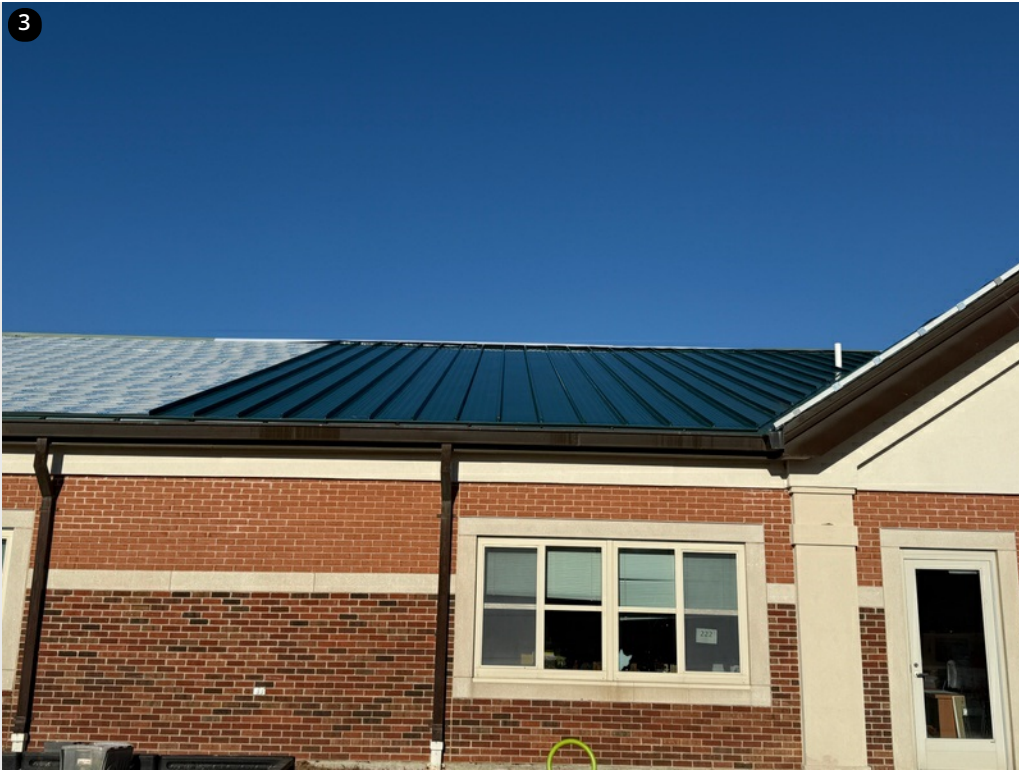


Panels installed Saturday- 11/30/24

4



Fasteners observed properly penetrating roof deck- 11/30/24

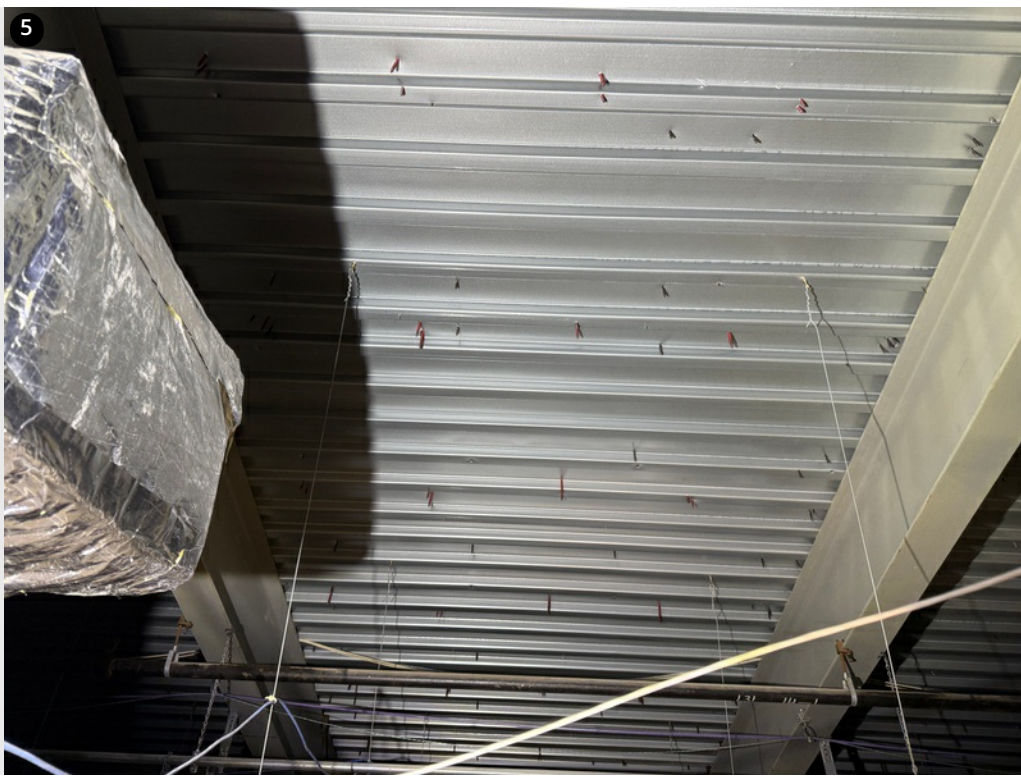

5 Fasteners observed properly penetrating roof deck- 11/30/24



6 Panels installed on dormers- Saturday 11/30/24

7



Crew installing panels on dormer- 12/2/24

8



Progress overview- 12/2/24

9

Progress overview- 12/2/24



10

Crew installing panels on dormer- 12/3/24



11



Crew fastening clips on field section behind copula- 12/4/24

12



Overview- Clip spacing on field area behind copula- 12/4/24


13

Overview- Clip spacing on field area behind copula- 12/4/24




14

Overview- Panels installed on dormer- 12/4/24

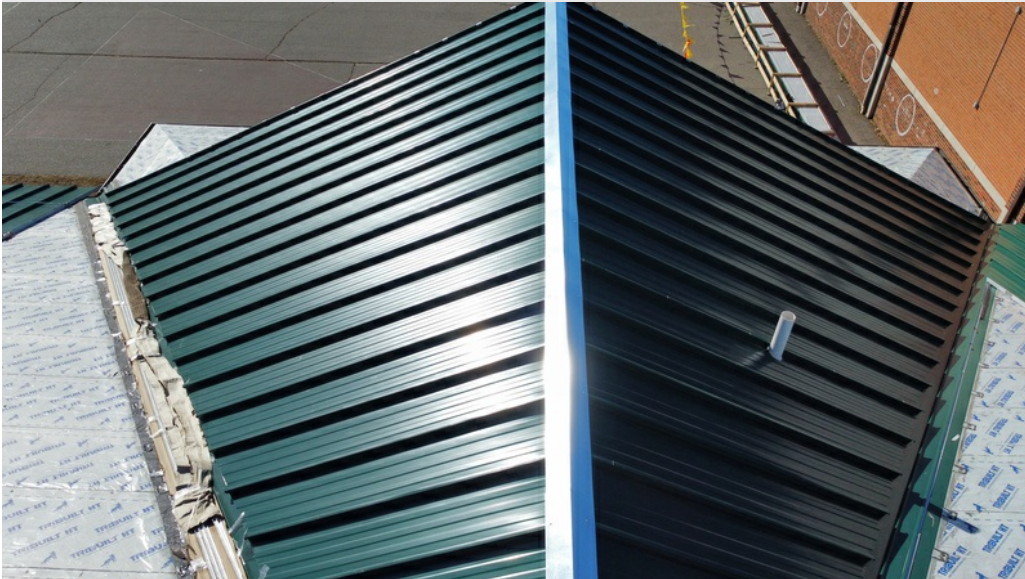

15

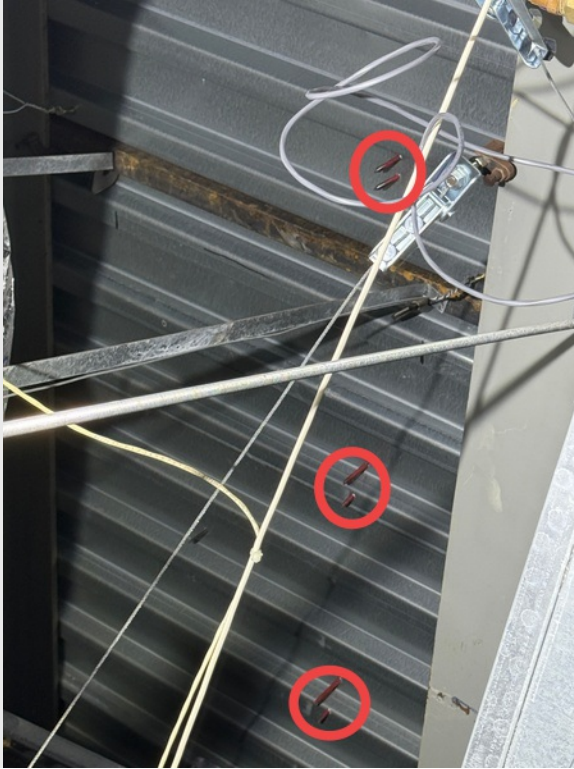

Fasteners on last panel installed observed properly penetrating deck- 12/4/24

16



Panels being installed on walkway roof- 12/6/24



17 Overview- Clip spacing- 12/6/24



18 Progress overview- 12/6/24
