Silver Petrucelli + Associates
3190 Whitney Avenue | Hamden CT 06518
311 State Street | New London CT 06320
203 230 9007 silverpetrucelli.com

Field Report

Field Report No.:	**13**

SP&A Project No: 22.331 **Report Date:** 11-15-2024 **Time:** 9:30AM

Project: *(Name & Location)*
Gales Ferry School
1854 CT-12
Gales Ferry, CT 06335

General Contractor:
The Imperial Company, Inc.

Weather				Site Conditions		Day of Week	
☐ Temp. Range: 63°				☒ Clear	☐ Dusty	☐ Monday	☐ Thursday
☒ Clear	☐ Rain	☐ Foggy	☐ Warm	☐ Muddy	☐ Windy	☐ Tuesday	☒ Friday
☐ Overcast	☐ Snow	☐ Cold	☐ Hot	☐ Other		☐ Wednesday	☐ Saturday

Type of Work Observed Being Performed

1	☐	Site work	7	☐	General Trades/Drywall	13	☐	Specialties/ Food Service	19	☐	Sprinkler
2	☐	Demolition	8	☐	Windows & Doors	14	☐	Elevators	20	☒	Finish metal
3	☐	Concrete	9	☐	Roofing	15	☐	Plumbing	21	☐	Iron workers
4	☐	Masonry	10	☐	Flooring	16	☐	HVAC	22	☐	Tester (Tri-state)
5	☐	Steel/Misc. Metals	11	☐	Pool	17	☐	Electrical	23	☐	Audio Vis/Low Volt
6	☐	Carpentry/Casework/ Mill Work	12	☐	Painting/Interior Finishes	18	☐	Temperature Controls/BMS	24	☐	Other:

Work Performed at time of site visit:

- Approximate number of workers on site – 5
- Installing the panels on the north side of roof A, to the left of the main entrance. See attached photos.

General Remarks:

- Crew will be working on Saturday (11/16).
- Work is to continue working east on the north roof A.
- IM is using red screws for easier identification for penetration thru the decking.
- As per the site meeting on Monday (11/11), Imperial is to remove the newly installed panels on the gym & the wing of roof A (in selected areas).
- Areas where the screws were removed and not placed back in the same hole, holes are being caulked.
- Roofer as now using 8" screws, except at the drip edges since there is blocking for the screws to grab.
- Installers have completed the valleys.
- For panels that meeting with the structure or valleys, (no full panels) have not been installed.
- Large panels are temporarily placed in place. Imperial has confirmed that they are secured.
- Screws depths were discussed and confirmed that the screws are penetrating the decking with the required under deck exposure.

Visitors:

- None.

Construction Administrator: Steven June *(Print Name)* _____ *(Signature)* 11/18/2024 *(Date)*

Copies To: ☐ CA ☐ Architect ☒ Contractor ☒ Owners

PHOTOS (see attached photos);

Silver Petrucelli + Associates
3190 Whitney Avenue | Hamden CT 06518
311 State Street | New London CT 06320
203 230 9007 silverpetrucelli.com

Roof A – North elevation looking southeast

Roof A – Overview looking east

Silver Petrucelli + Associates
3190 Whitney Avenue | Hamden CT 06518
311 State Street | New London CT 06320
203 230 9007 silverpetrucelli.com

Roof A – Panels to be fastened in other areas

Roof A – Overview of the west elevation

Silver Petrucelli + Associates
3190 Whitney Avenue | Hamden CT 06518
311 State Street | New London CT 06320
203 230 9007 silverpetrucelli.com

Roof A – Caulking of the clips

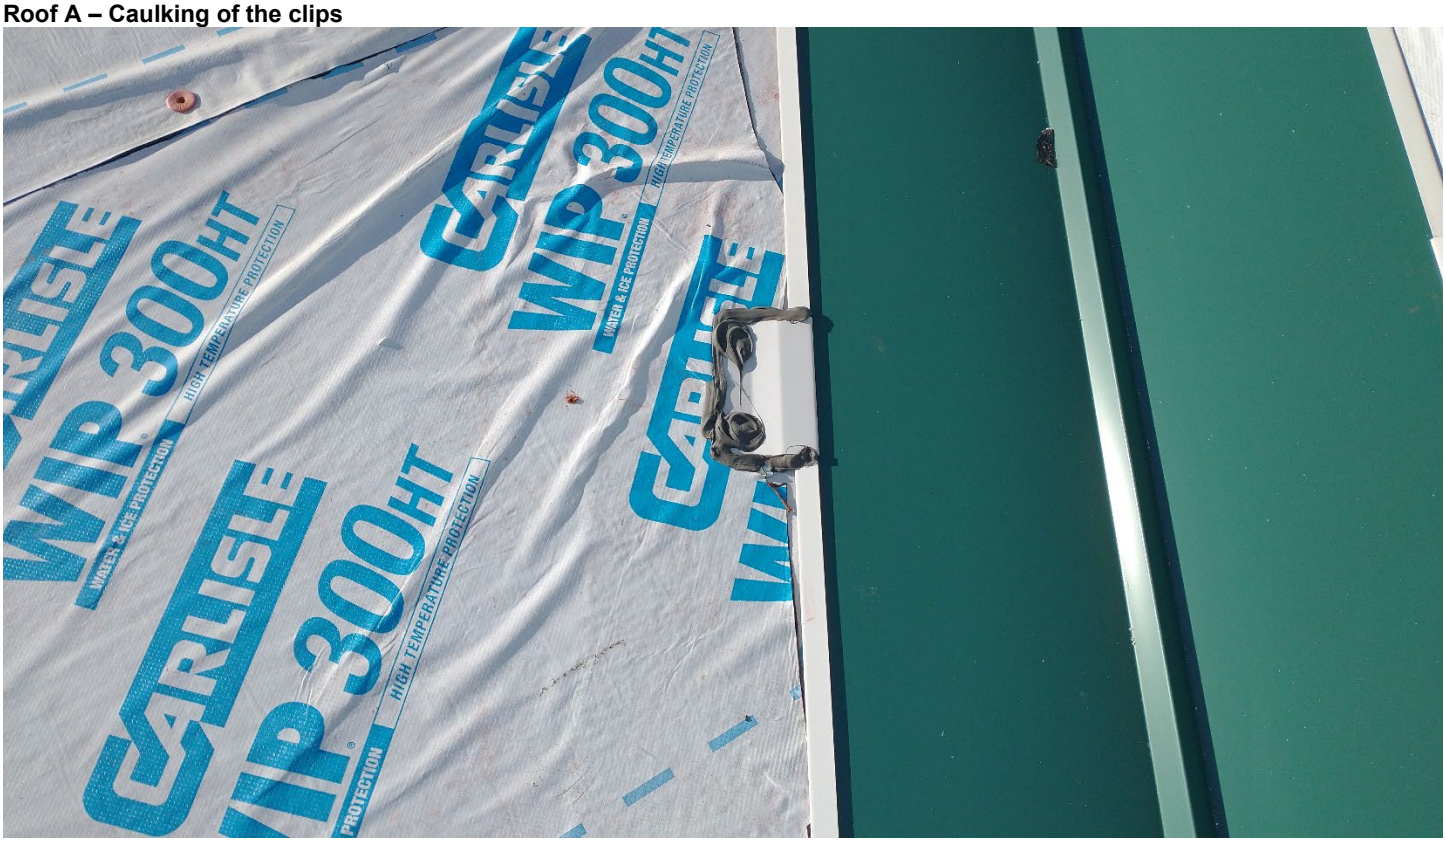
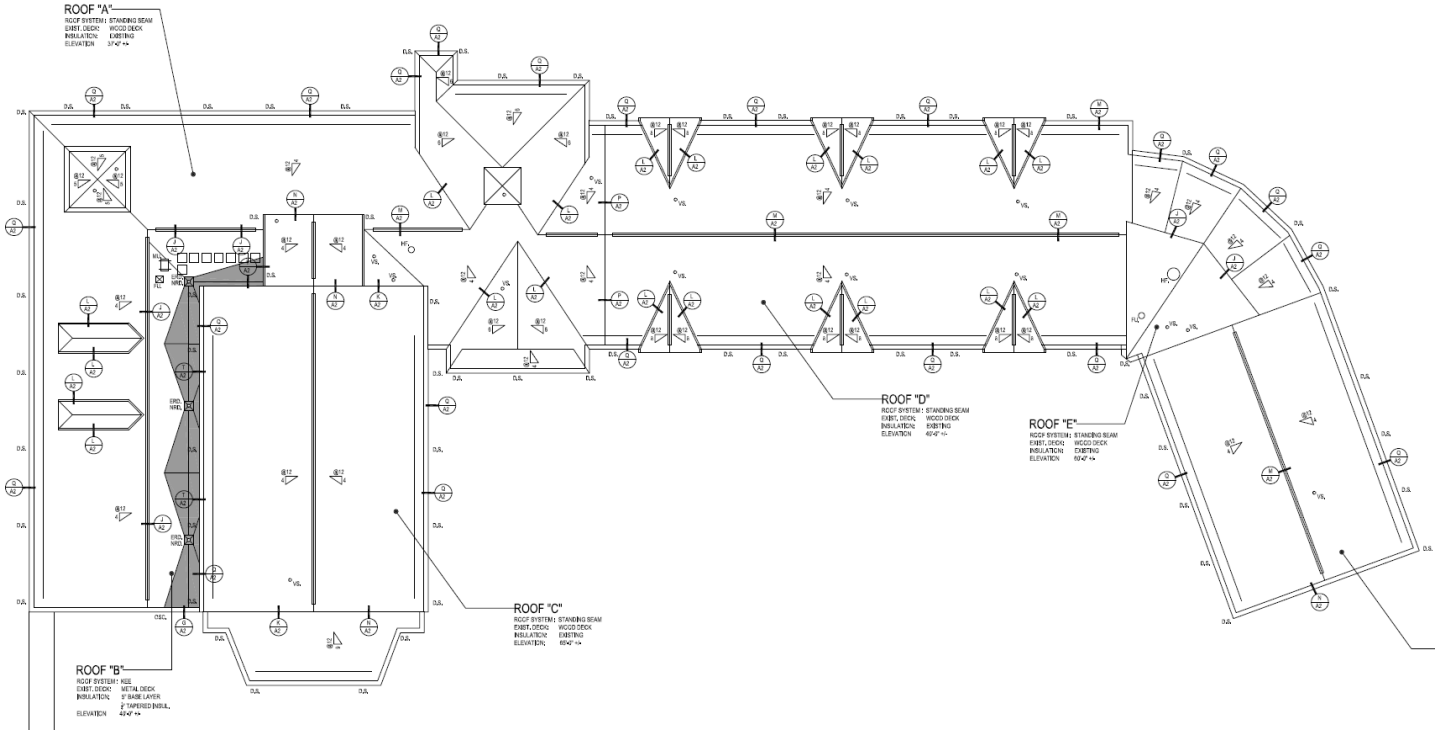
Roof plan
